


Project: Alberta Oil and Gas Facility Expansion
Report Date: 6-Mar-26
Data Source: Primavera P6 Schedule & Excel Earned Value Analysis

Metric:	
BAC (Budget at Completion)	\$73,608,565.00
PV (Planned Value)	\$73,144,430.00
EV (Earned Value)	\$72,978,010.41
AC (Actual Cost)	\$72,935,840.00
CPI (Cost Performance Index)	1.001
SPI (Schedule Performance Index)	0.998
Cost Variance	\$42,170.41
Schedule Variance	-\$166,419.59
EAC (Estimate at Completion)	\$73,566,030.23

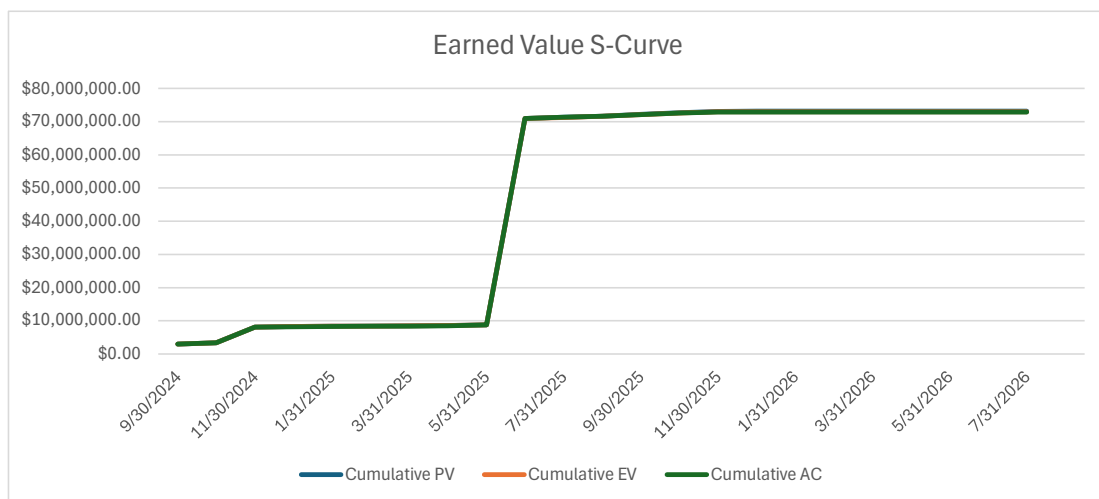

As of 03/06/2026 the project is slightly behind schedule but essentially on budget. Planned Value (PV) is \$73.14M, Earned Value (EV) is \$72.98M, and Actual Cost (AC) is \$72.94M. This results in a CPI of 1.00, indicating cost performance is effectively on plan, and an SPI of 1.00 (slightly below 1.0), indicating minor schedule slippage. The current variances are CV = +\$42k and SV = -\$166k, so the project has earned marginally less work than planned by the data date, but at essentially the expected cost. The main schedule impact remains the earlier civil/construction delay, which pushed downstream activities, while cost performance appears stable because major spending has tracked closely with earned progress under the current reporting assumptions.
